





SEASIDE SCHOOL BOND



PROJECT UPDATE



PROJECT DASHBOARD

	BUDGET	SCHEDULE	SCOPE	COMMUNITY
Monthly Rating				



ON TARGET








CAUTION



BEHIND

NOVEMBER 2020 MILESTONES

-  PRES – Gearhart play structure relocation underway
-  PRES – Modular 5 completed and punchlist
-  PRES – Punchlist work near completion
-  PRES – Classroom Ceiling tile work complete
-  HSMS Weather Barrier Remediation – Successful inspection and testing of west side installation

DECEMBER 2020 TARGET MILESTONES



PRES – Cafeteria Ceiling Tile work



PRES – Complete additional work



HSMS – Relocate Booster Club sign from SHS



HSMS – Complete Punchlist and additional work



HSMS – Continue Weather Barrier Remediation, begin masonry install on west facade

EXECUTIVE SUMMARY

CONSTRUCTION – MIDDLE AND HIGH SCHOOL

- Site – Storm drainage work
- Site – Finish Landscaping work in the Spring
- Facade – Weather Barrier Remediation to continue through February
- Interior – Wrapping up last of punchlist items
- Interior – Finishing up building commissioning
- Interior – completing added work
- Technology – Wrapping up security, data and exterior door controls




EXECUTIVE SUMMARY

CONSTRUCTION – PACIFIC RIDGE

- Site – Gearhart Play equipment relocation
- Interior – Wrapping up last of punchlist items
- Interior – Finishing up building commissioning
- Interior – completing added work
- Technology – Wrapping up security, data and exterior door controls



BUDGET

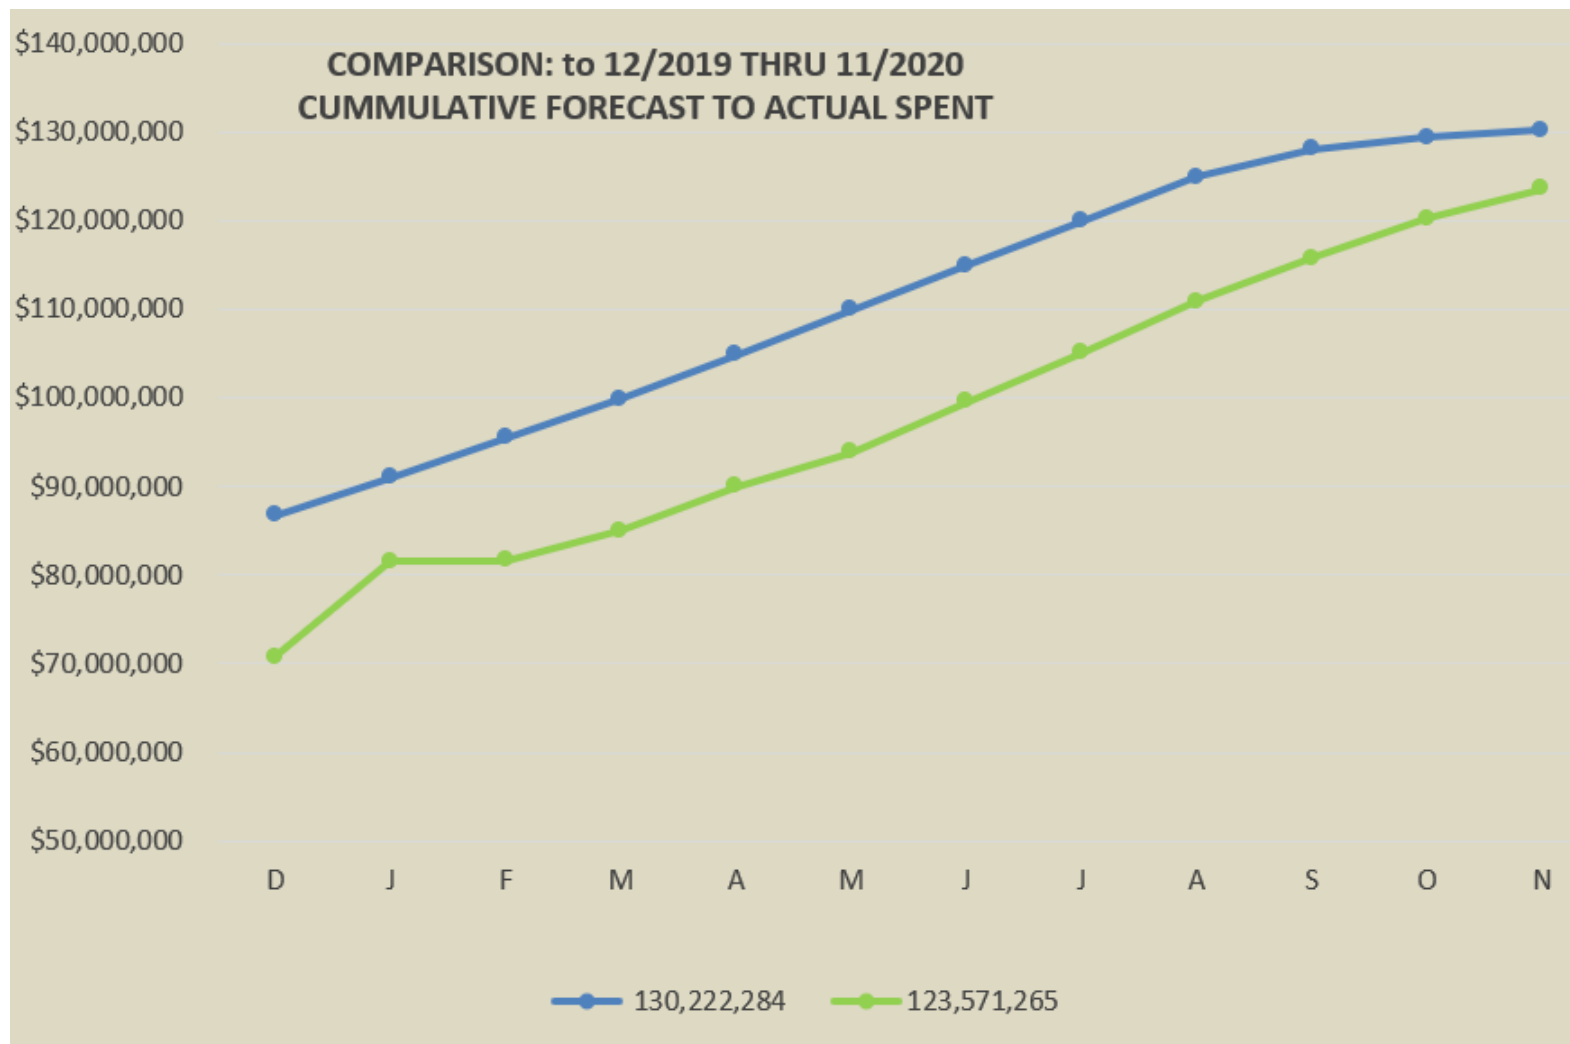



QUESTIONS?
