

# SEASIDE SCHOOLS

---

## CONSTRUCTION PROJECT





APRIL 2020

### MONTHLY PROGRESS REPORT



### PROJECT DASHBOARD

PROJECT:	SEASIDE SCHOOL DISTRICT 2017 GO BOND PROJECT
MONTH OF:	APRIL 2020
PREPARED FOR:	SEASIDE SCHOOL DISTRICT
PREPARED BY:	JIM HENRY, DAY CPM PROJECT MANAGER
OWNER's REPRESENTATIVE:	DAY CPM
ARCHITECT:	BRIC ARCHITECTURE INC.
CM/GC:	HOFFMAN CONSTRUCTION COMPANY OF OREGON

	BUDGET	SCHEDULE	SCOPE	COMMUNITY
Monthly Rating				



ON TARGET








CAUTION








BEHIND

### APRIL 2020 MILESTONES

-  Completed furniture scope
-  Water connection to City water for building testing and commissioning
-  Temporary Gym at the Heights surplus to Clatsop County for 4H / FFA use
-  Renovation work commenced in all areas of the Heights, including roofing
-  MS/HS windows and window testing complete

### MAY 2020 TARGET MILESTONES

-  Complete Middle School wing interior
-  Purge and pack both SHS and Broadway MS for summer move
-  Contract moving company for SHS, BMS, GES and District Office move
-  Pave access road between HES and the HS / MS
-  Plant grass at new athletic field



## EXECUTIVE SUMMARY

### CONSTRUCTION

- Work proceeding at HS/MS:
  - Site – grading in west parking
  - Site – continue paving
  - Site – athletic field soil and planting
  - Kitchen and Culinary Arts equipment installation
  - Painting gym floor
  - Drywall and painting
  - Ceiling grid installation
  - Interior painting
  - Classroom cabinets and flooring installation
- Work at Seaside Heights
  - Demolition in all existing school areas
  - Plumbing rough-in both new and lead pipe replacement
  - Data and Electrical installation
  - Mechanical Rough-in ongoing
  - Prep work for new VCT flooring and carpet

### CITY OF SEASIDE:

- Construction Coordination - Seaside Public Works:
  - Pump station
    - CMU walls up
    - Underground piping complete
  - Reservoir
    - Reservoir tank fabrication complete
    - Tank interior painting underway



### PROJECT BUDGET:

- Budget:
  - Heights – interior work underway in all pods. Additional abatement costs associated with replacing original vinyl flooring
  - HS MS – unknown risks minimized at this point in the project





▪ **BUDGET:**

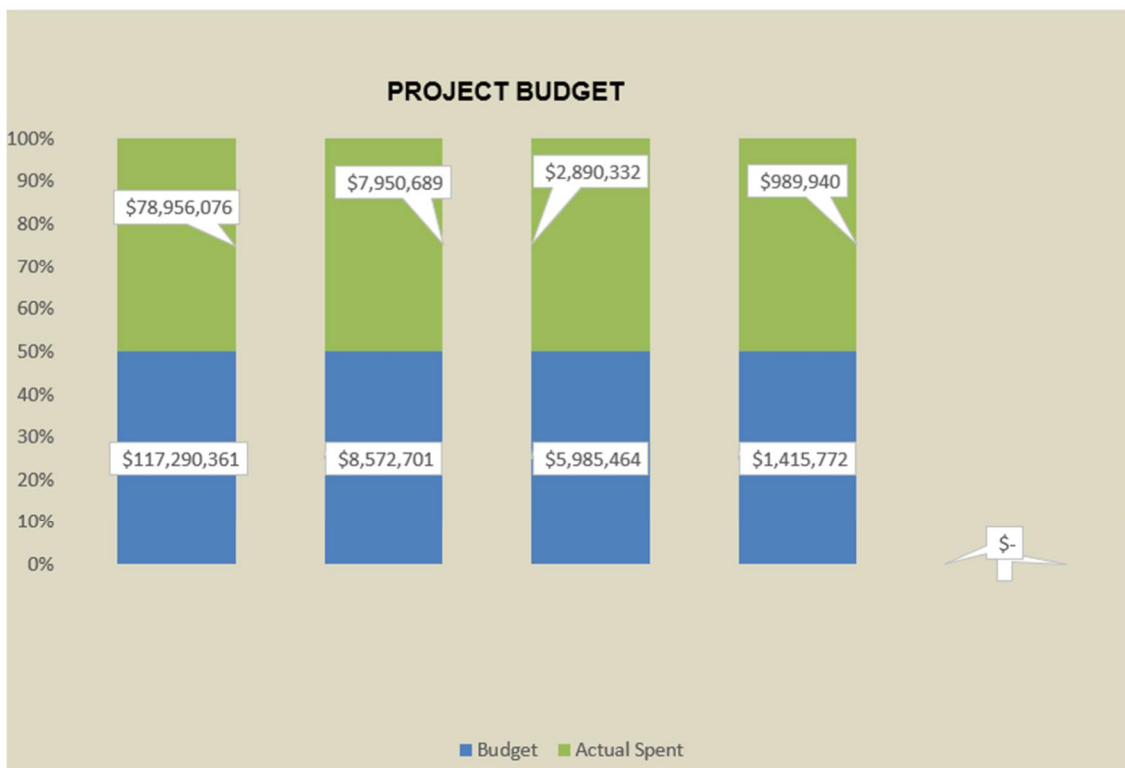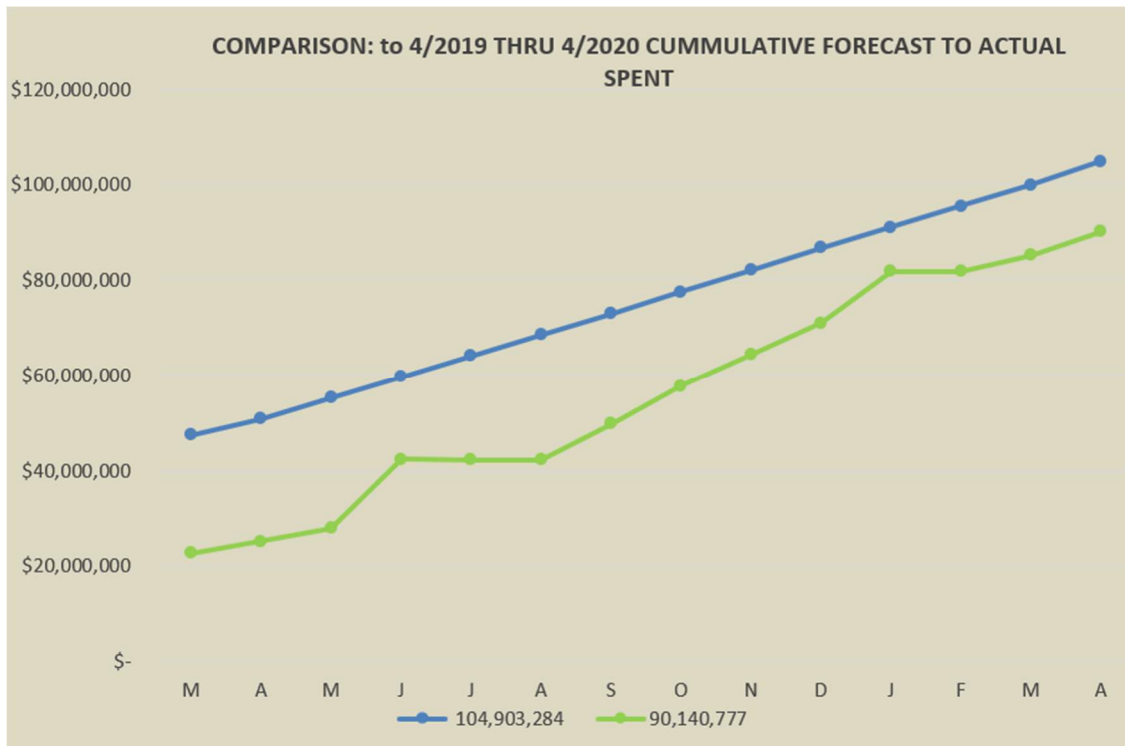

**END OF REPORT**
